


Road Update #5
Canyon Woods Reconstruction
7.7.2021

The following is the most current progress schedule as of July 7, 2021. Note- work is weather dependent. We will continue to provide additional updates through the portable changeable message sign and through your HOA. Continue to expect delays while this project continues.

- Thursday, July 8th – Drainage work along the perimeter of the roadway will start. Access to driveways will be maintained.
- Friday, July 9th thru Monday, July 12th – Stone road base material will be placed over entire roadbed. Overnight access to driveways will be maintained.
- Tuesday, July 13th thru Thursday, July 15th – Concrete curb installation along Phase I (RED Line – See attached map) - Access to driveways will be restricted. We are asking residents to work with neighbors not effected by the phase during concrete pours (day time hours). Parking in roadway during placement of concrete will be restricted. Access to driveways will be restricted. Until temporary ramps have been reestablished.
- Monday, July 19th thru Wednesday, July 21st - Concrete curb installation along Phase II (BLUE Line – See attached map) - Access to driveways will be restricted. We are asking residents to work with neighbors not effected by the phase during concrete pours (day time hours). Parking in roadway during placement of concrete will be restricted. Access to driveways will be restricted. Until temporary ramps have been reestablished.

Handwritten: Phase I

Handwritten: Phase II

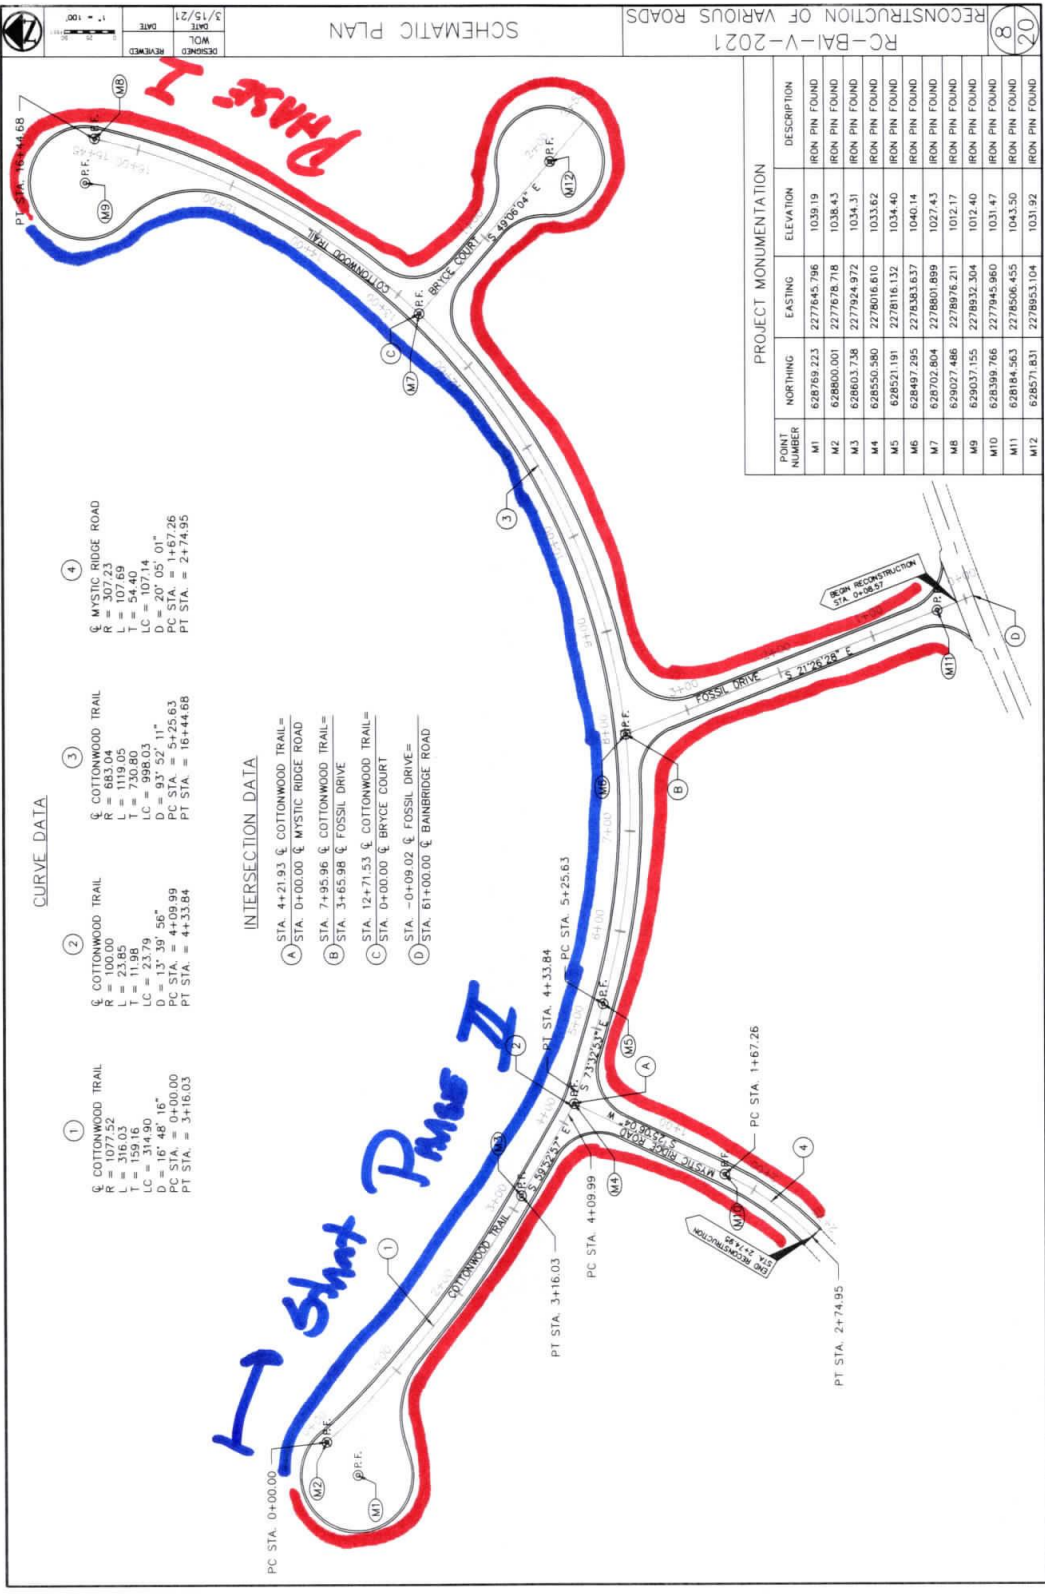

SCHMATIC PLAN

RC-BAI-V-2021
RECONSTRUCTION OF VARIOUS ROADS

3/15/21
WCL
DATE
3/15/21

20
8
